


ID	Task Mode	WBS	Task Name	Cost	Duration	Start	April 2023								
							17	22	27	1	6	11	16	21	2
1		1	შავი კაჩკახი	€ 248,854.60	72 days?	Mon 3/27/23									
2		1.1	მინის სამუშაოები	€ 8,994.14	11 days	Mon 3/27/23									
3		1.1.1	სამშენებლო მოედნის მომზადება	€ 0.00	1 wk	Mon 3/27/23									
4		1.1.2	დაბეგმვა/მომზადება	€ 287.30	4 days	Mon 3/27/23									
5		1.1.3	დაკვანძვა	€ 600.00	0.5 days	Tue 3/28/23									
6		1.1.4	მინის მოჭრა-გატანა	€ 5,820.00	7.5 days	Tue 3/28/23									
7		1.1.5	ბელოუსტილის დაგება	€ 25.84	1 hr	Fri 4/7/23									
8		1.1.6	ბადასტის დაყრა-დატყვევნა	€ 2,261.00	1 day	Fri 4/7/23									
9		1.1.7	მინის სამუშაოების ბუფერი	€ 0.00	1 day	Mon 4/10/23									
10		1.1.8	მინის სამუშაოების ჩაბახება	€ 0.00	0 days	Mon 4/10/23									
11		1.2	ფუნდამენტის ფილა	€ 35,981.83	12 days	Mon 4/3/23									
12		1.2.1	მომზადება	€ 23,731.53	5 days	Mon 4/3/23									
13		1.2.2	დაკვანძვა	€ 600.00	0.5 days	Mon 4/3/23									
14		1.2.3	სამატილის მოწვნა	€ 0.00	2 days	Tue 4/11/23									
15		1.2.4	ჩაჩრვების მოწყობა	€ 0.00	1 day	Thu 4/13/23									
16		1.2.5	ბეტონის დასხმა	€ 11,650.30	1 day	Tue 4/18/23									
17		1.2.6	ჩაჩრვების მოხსნა	€ 0.00	1 day	Wed 4/19/23									
18		1.2.7	ფუნდამენტის ბუფერი	€ 0.00	1 day	Thu 4/20/23									
19		1.2.8	ფუნდამენტის ჩაბახება	€ 0.00	0 days	Thu 4/20/23									
20		1.3	სახურელი -1	€ 23,786.10	33 days	Mon 4/10/23									
21		1.3.1	მომზადება -1	€ 773.51	8 days	Mon 4/10/23									
22		1.3.2	დაკვანძვა	€ 600.00	0.5 days	Mon 4/10/23									
23		1.3.3	ვეტიკალის მოქმედა -1	€ 0.00	5 days	Fri 4/21/23									

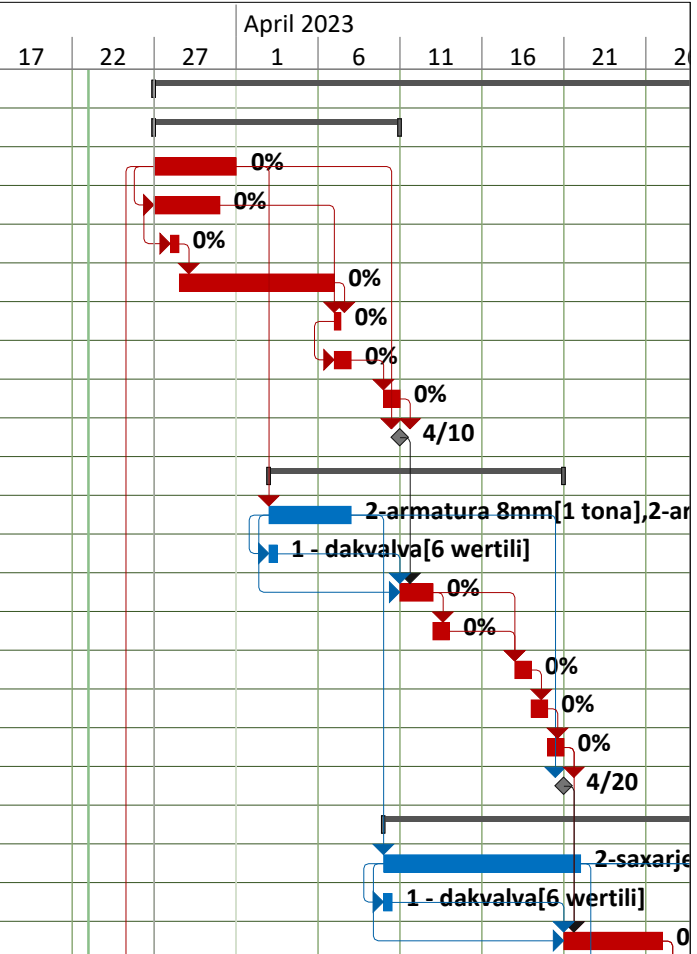

Project: msproj11 Date: Thu 3/23/23	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Critical	
	Project Summary		Duration-only		Critical Split	
	External Tasks		Manual Summary Rollup		Progress	
	External Milestone		Manual Summary		Manual Progress	

ID	Task Mode	WBS	Task Name	Cost	Duration	Start	April 2023											
							17	22	27	1	6	11	16	21	2			
24		1.3.4	ჩაჩქარების მონაცემები -1	0.00	1 day	Thu 4/27/23												
25		1.3.5	ბუჯეტის ჩახედვა -1	9,489.20	1 day	Fri 4/28/23												
26		1.3.6	შრომები -1	0.00	2 edays	Fri 4/28/23												
27		1.3.7	ჩაჩქარების მონაცემები -1	0.00	1 day	Mon 5/1/23												
28		1.3.8	აღჭრის მონაცემები	2,915.52	4 days	Thu 4/27/23												
29		1.3.9	ფორმის ჩაჩქარების მონაცემები - 0	0.00	1 day	Tue 5/2/23												
30		1.3.10	ფორმის მოქმედება - 0	0.00	2 days	Wed 5/3/23												
31		1.3.11	ბუჯეტის ჩახედვა - 0	10,007.86	1 day	Fri 5/5/23												
32		1.3.12	შრომები - 0	0.00	14 edays	Fri 5/5/23												
33		1.3.13	ჩაჩქარების მონაცემები - 0	0.00	1 day	Sat 5/20/23												
34		1.3.14	ბუჯეტი -1	0.00	2 days	Mon 5/22/23												
35		1.3.15	ფორმის ჩაბრუნება - 0	0.00	0 days	Tue 5/23/23												
36		1.4	საბოლოო +1	13,842.62	36 days	Sat 4/22/23												
37		1.4.1	მომზადება +1	773.51	15 days	Sat 4/22/23												
38		1.4.2	დაჯერება	600.00	0.5 days	Sat 4/22/23												
39		1.4.3	სვეტების მოქმედება +1	0.00	1 day	Mon 5/8/23												
40		1.4.4	ჩაჩქარების მონაცემები +1	0.00	1 day	Wed 5/10/23												
41		1.4.5	ბუჯეტის ჩახედვა +1	1,037.33	1 day	Thu 5/11/23												
42		1.4.6	შრომები+1	0.00	1 eday	Thu 5/11/23												
43		1.4.7	აღჭრის მონაცემები	1,423.92	3 days	Tue 5/9/23												
44		1.4.8	ჩაჩქარების მონაცემები+1	0.00	1 day	Sat 5/13/23												
45		1.4.9	ფორმის ჩაჩქარების მონაცემები +1	0.00	2 days	Mon 5/15/23												
46		1.4.10	ფორმის მოქმედება +1	0.00	2 days	Wed 5/17/23												

Project: msproj11
Date: Thu 3/23/23

Task		Inactive Task		Start-only	
Split		Inactive Milestone		Finish-only	
Milestone		Inactive Summary		Deadline	
Summary		Manual Task		Critical	
Project Summary		Duration-only		Critical Split	
External Tasks		Manual Summary Rollup		Progress	
External Milestone		Manual Summary		Manual Progress	

ID	Task Mode	WBS	Task Name	Cost	Duration	Start	April 2023								
							17	22	27	1	6	11	16	21	2
47		1.4.11	ფილის ბუკონის დასება +1	€ 10,007.86	1 day	Fri 5/19/23									
48		1.4.12	ფილის შიშობა +1	€ 0.00	14 edays	Fri 5/19/23									
49		1.4.13	ფილის ჩაჩრეობის მონხნა +1	€ 0.00	1 day	Sat 6/3/23									
50		1.4.14	ბუფეჩი +1	€ 0.00	2 days	Mon 6/5/23									
51		1.4.15	ფილის ჩაბაჩება +1	€ 0.00	0 days	Tue 6/6/23									
52		1.5	სახორეი +2	€ 21,043.34	40 days	Mon 5/1/23									
53		1.5.1	მომახაგება +2	€ 1,547.02	10 days	Sat 5/20/23									
54		1.5.2	დავდაცა	€ 600.00	0.5 days	Sat 5/20/23									
55		1.5.3	სვეტების მოქსოვა +2	€ 0.00	1 day	Tue 5/23/23									
56		1.5.4	ჩაჩრეობის მონეობა +2	€ 0.00	1 day	Wed 5/24/23									
57		1.5.5	ბუკონის დასება +2	€ 1,037.33	1 day	Thu 5/25/23									
58		1.5.6	შიშობა +2	€ 0.00	1 eday	Thu 5/25/23									
59		1.5.7	აღჭეჩვილობა	€ 1,423.92	3 days	Wed 5/24/23									
60		1.5.8	ჩაჩრეობის მონხნა +2	€ 0.00	1 day	Sat 5/27/23									
61		1.5.9	ფილის ცაჩრეობის მონეობა +2	€ 0.00	2 days	Mon 5/29/23									
62		1.5.10	ფილის მოქსოვა +2	€ 0.00	2 days	Wed 5/31/23									
63		1.5.11	ფილის ბუკონის დასება +2	€ 10,007.86	1 day	Fri 6/2/23									
64		1.5.12	ფილის შიშობა +2	€ 0.00	14 edays	Fri 6/2/23									
65		1.5.13	ფილის ჩაჩრეობის მონხნა +2	€ 0.00	1 day	Sat 6/17/23									
66		1.5.14	ბუფეჩი +2	€ 0.00	2 days	Mon 6/19/23									
67		1.5.15	აღჭეჩვილობის უხეწვეცეოტა	€ 6,427.20	48 edays	Mon 5/1/23									
68		1.5.16	ფილის ჩაბაჩება +2	€ 0.00	0 days	Tue 6/20/23									
69		1.6	სადიხველის იზომდაცო	€ 5,463.70	7 days	Tue 5/2/23									

Project: msproj11
Date: Thu 3/23/23

Task		Inactive Task		Start-only	
Split		Inactive Milestone		Finish-only	
Milestone		Inactive Summary		Deadline	
Summary		Manual Task		Critical	
Project Summary		Duration-only		Critical Split	
External Tasks		Manual Summary Rollup		Progress	
External Milestone		Manual Summary		Manual Progress	

ID	Task Mode	WBS	Task Name	Cost	Duration	Start	April 2023								
							17	22	27	1	6	11	16	21	2
70		1.6.1	მომსახურება ბლოკი	ლ 1,583.70	1 wk	Tue 5/2/23									
71		1.6.2	მონყობა	ლ 3,880.00	2 days	Mon 5/8/23									
72		1.7	ბლოკის სამუშაოები	ლ 26,292.80	19 days	Sat 6/3/23									
73		1.7.1	მომსახურება ბლოკი	ლ 11,472.80	3 days	Sat 6/3/23									
74		1.7.2	ბლოკის მონყობა - 1	ლ 7,410.00	5 days	Wed 6/7/23									
75		1.7.3	ბლოკის მონყობა - 2	ლ 7,410.00	5 days	Mon 6/19/23									
76		1.7.4	ბლოკის ბუფერი	ლ 0.00	1 day	Sat 6/24/23									
77		1.7.5	ბლოკის ჩაბაზება	ლ 0.00	0 days	Sat 6/24/23									
78		1.8	კახ-ფანჯარა	ლ 26,730.79	21 days	Sat 6/3/23									
79		1.8.1	მომსახურება-ფანჯარა	ლ 1,086.60	5 days	Sat 6/3/23									
80		1.8.2	კახფანჯარის მონყაფი	ლ 19,747.84	1 day	Mon 6/26/23									
81		1.8.3	მომსახურება ხუნის კახი	ლ 2,712.00	5 days	Sat 6/3/23									
82		1.8.4	ხუნის კახის მონყაფი	ლ 387.60	1 day	Mon 6/26/23									
83		1.8.5	ხუნის მომსახურება	ლ 0.00	2 days	Wed 6/7/23									
84		1.8.6	ხუნის დამზადება	ლ 0.00	5 days	Thu 6/8/23									
85		1.8.7	ხუნის მონყაფი	ლ 2,796.75	1 day	Wed 6/14/23									
86		1.8.8	კახფანჯარის ბუფერი	ლ 0.00	1 day	Tue 6/27/23									
87		1.8.9	ჩაბაზება	ლ 0.00	0 days	Tue 6/27/23									
88		1.9	ზედნადები & გადასახადები	ლ 86,719.28	72 days?	Mon 3/27/23									
89		1.9.1	ჰიოქტის დანყება	ლ 0.00	0 days	Mon 3/27/23									
90		1.9.2	ჰიოქტის დახუნება	ლ 0.00	0 days	Tue 6/27/23									
91		1.9.3	მუნეჰმუნტი	ლ 16,289.28	72 days?	Mon 3/27/23									
92		1.9.4	გაუთვარისნუნებელი	ლ 8,960.00	72 days?	Mon 3/27/23									


Project: msproj11
Date: Thu 3/23/23

Task		Inactive Task		Start-only	
Split		Inactive Milestone		Finish-only	
Milestone		Inactive Summary		Deadline	
Summary		Manual Task		Critical	
Project Summary		Duration-only		Critical Split	
External Tasks		Manual Summary Rollup		Progress	
External Milestone		Manual Summary		Manual Progress	


ID	Task Mode	WBS	Task Name	Cost	Duration	Start	April 2023									
							17	22	27	1	6	11	16	21	2	
93		1.9.5	მომგები	€ 23,400.00	72 days?	Mon 3/27/23										
94		1.9.6	ღწბ	€ 38,070.00	72 days?	Mon 3/27/23										




Project: msproj11 Date: Thu 3/23/23	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Critical	
	Project Summary		Duration-only		Critical Split	
	External Tasks		Manual Summary Rollup		Progress	
	External Milestone		Manual Summary		Manual Progress	

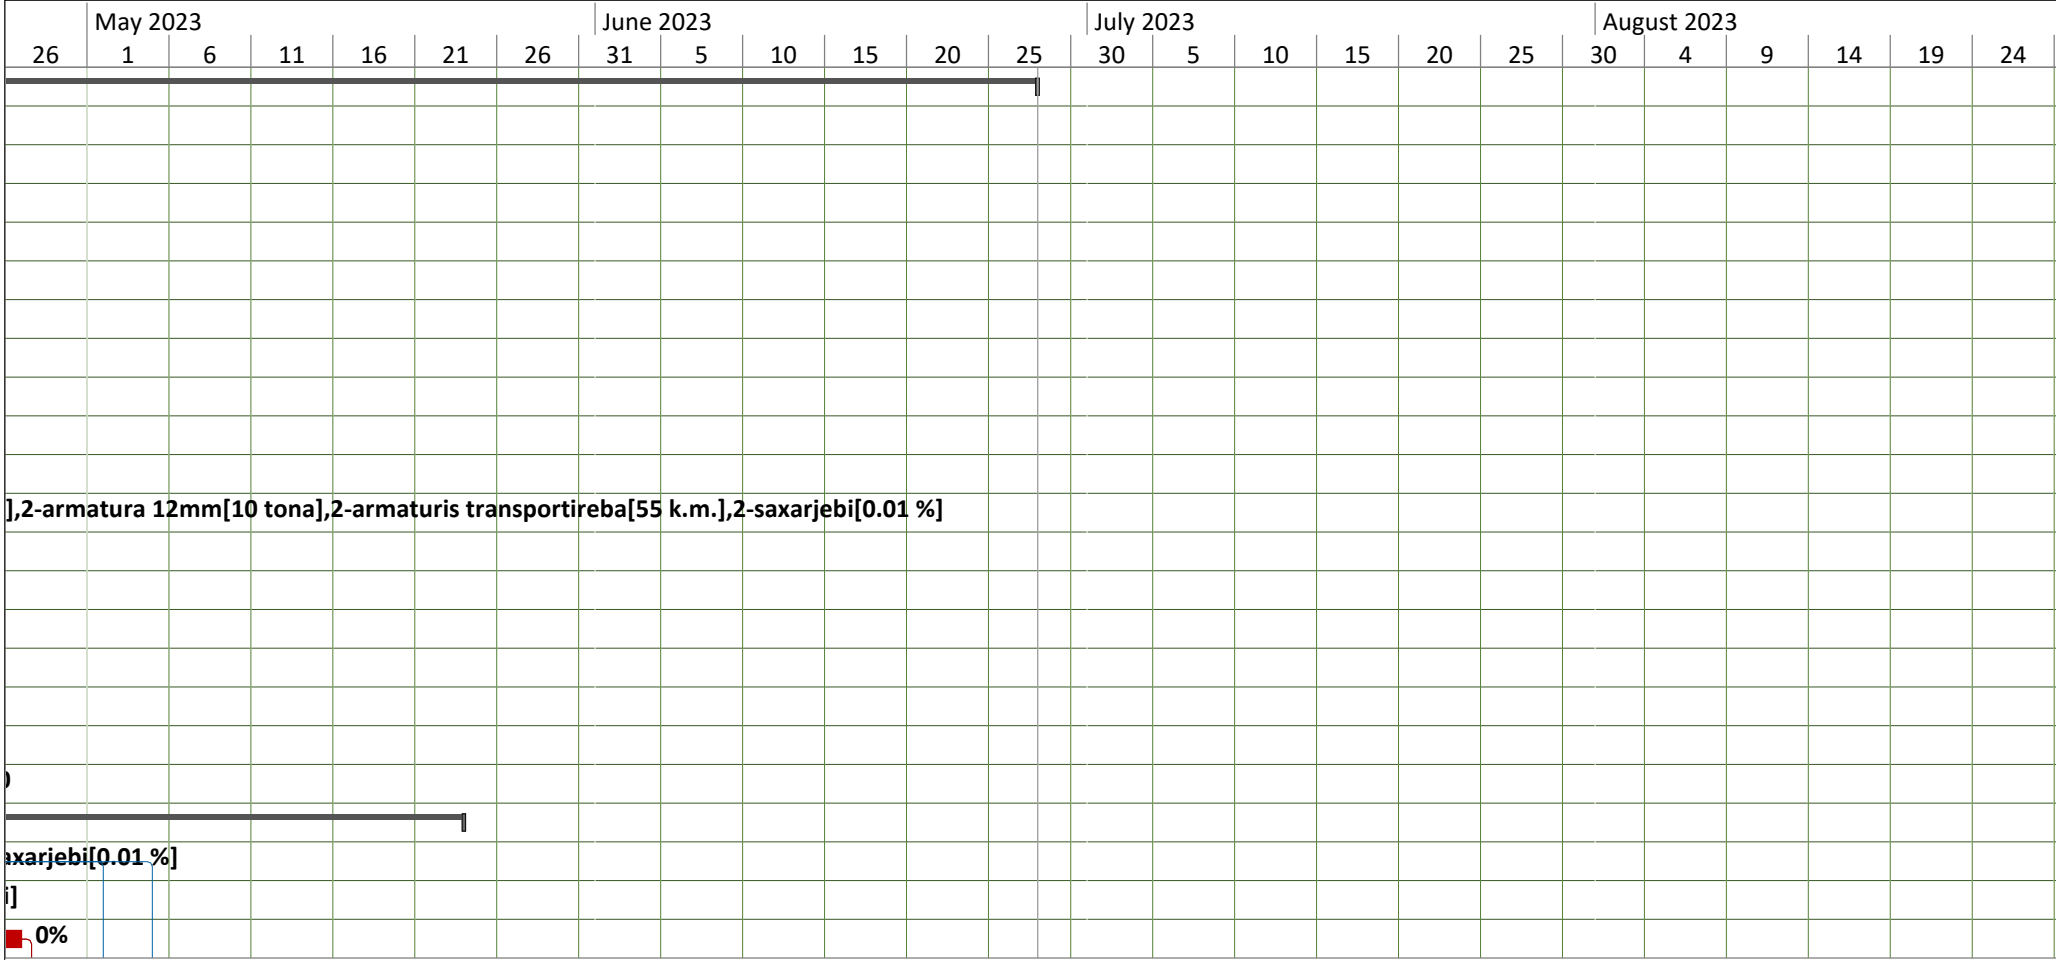

Project: msproj11 Date: Thu 3/23/23	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Critical	
	Project Summary		Duration-only		Critical Split	
	External Tasks		Manual Summary Rollup		Progress	
	External Milestone		Manual Summary		Manual Progress	

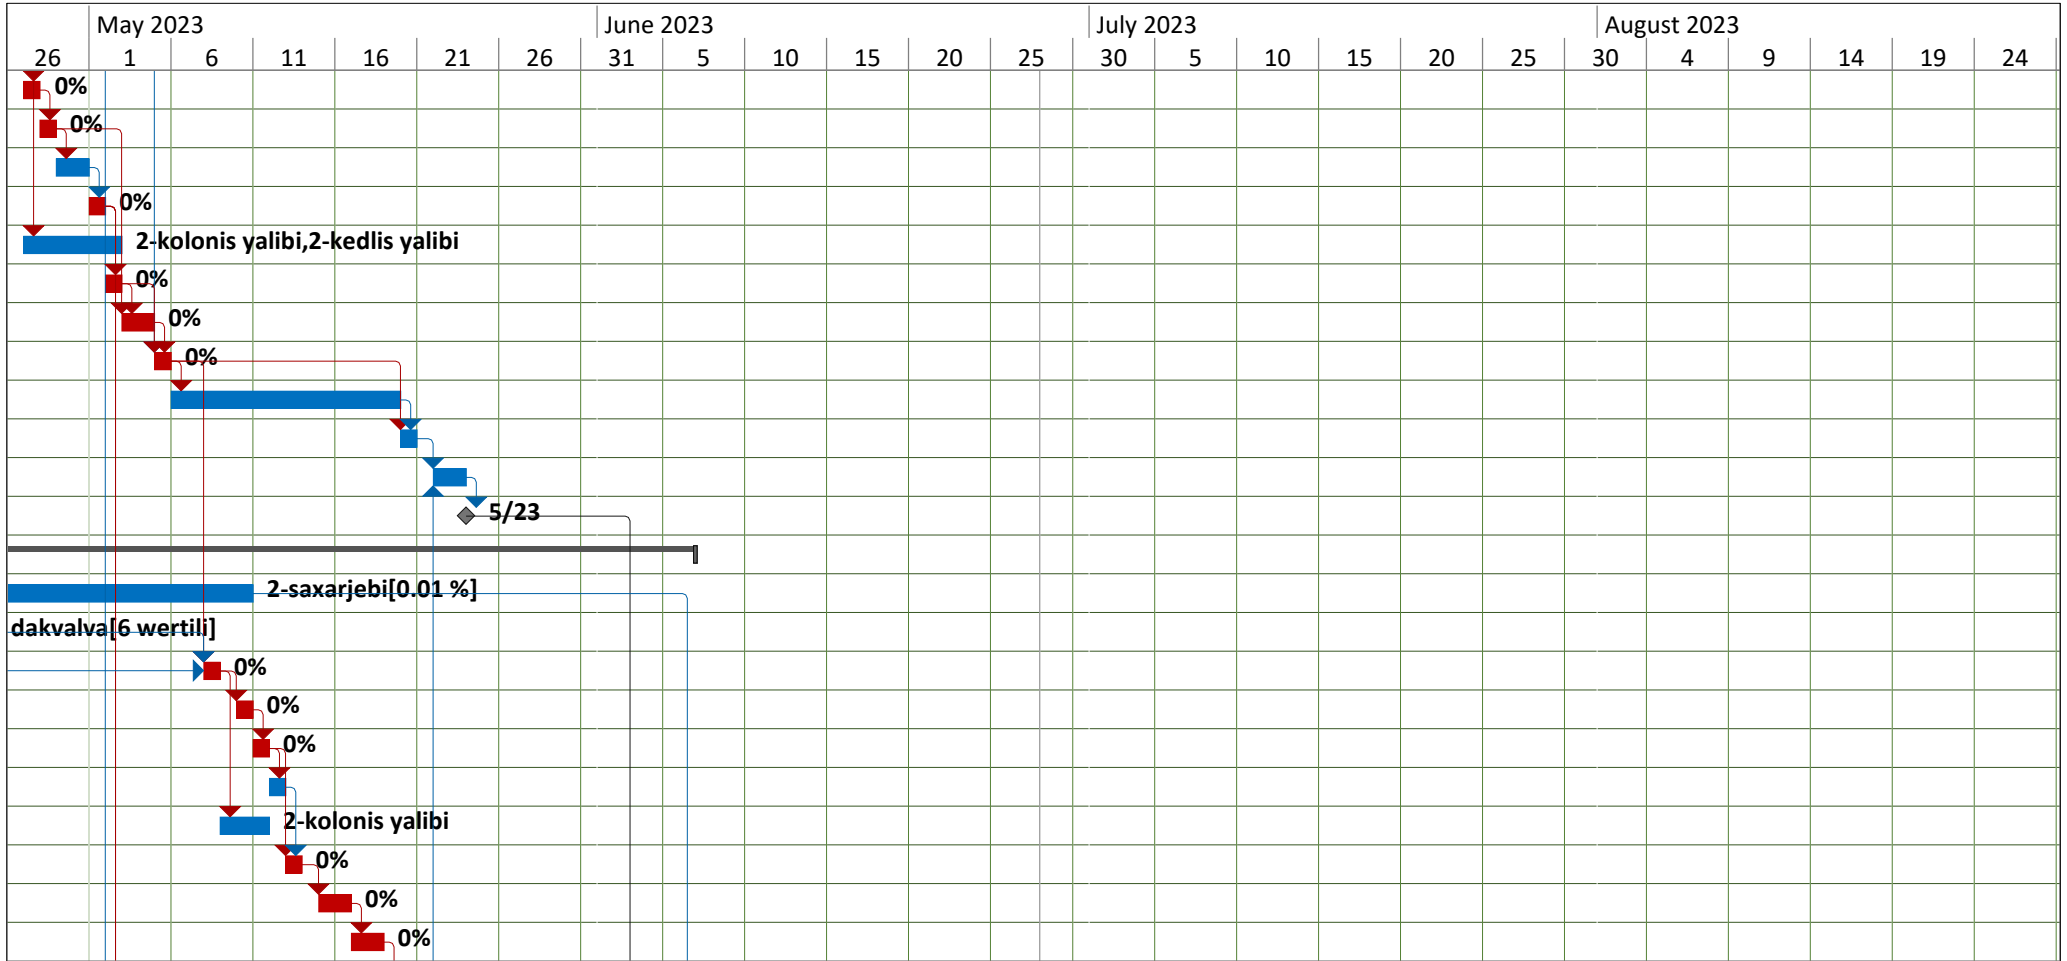


Project: msproj11 Date: Thu 3/23/23	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Critical	
	Project Summary		Duration-only		Critical Split	
	External Tasks		Manual Summary Rollup		Progress	
	External Milestone		Manual Summary		Manual Progress	

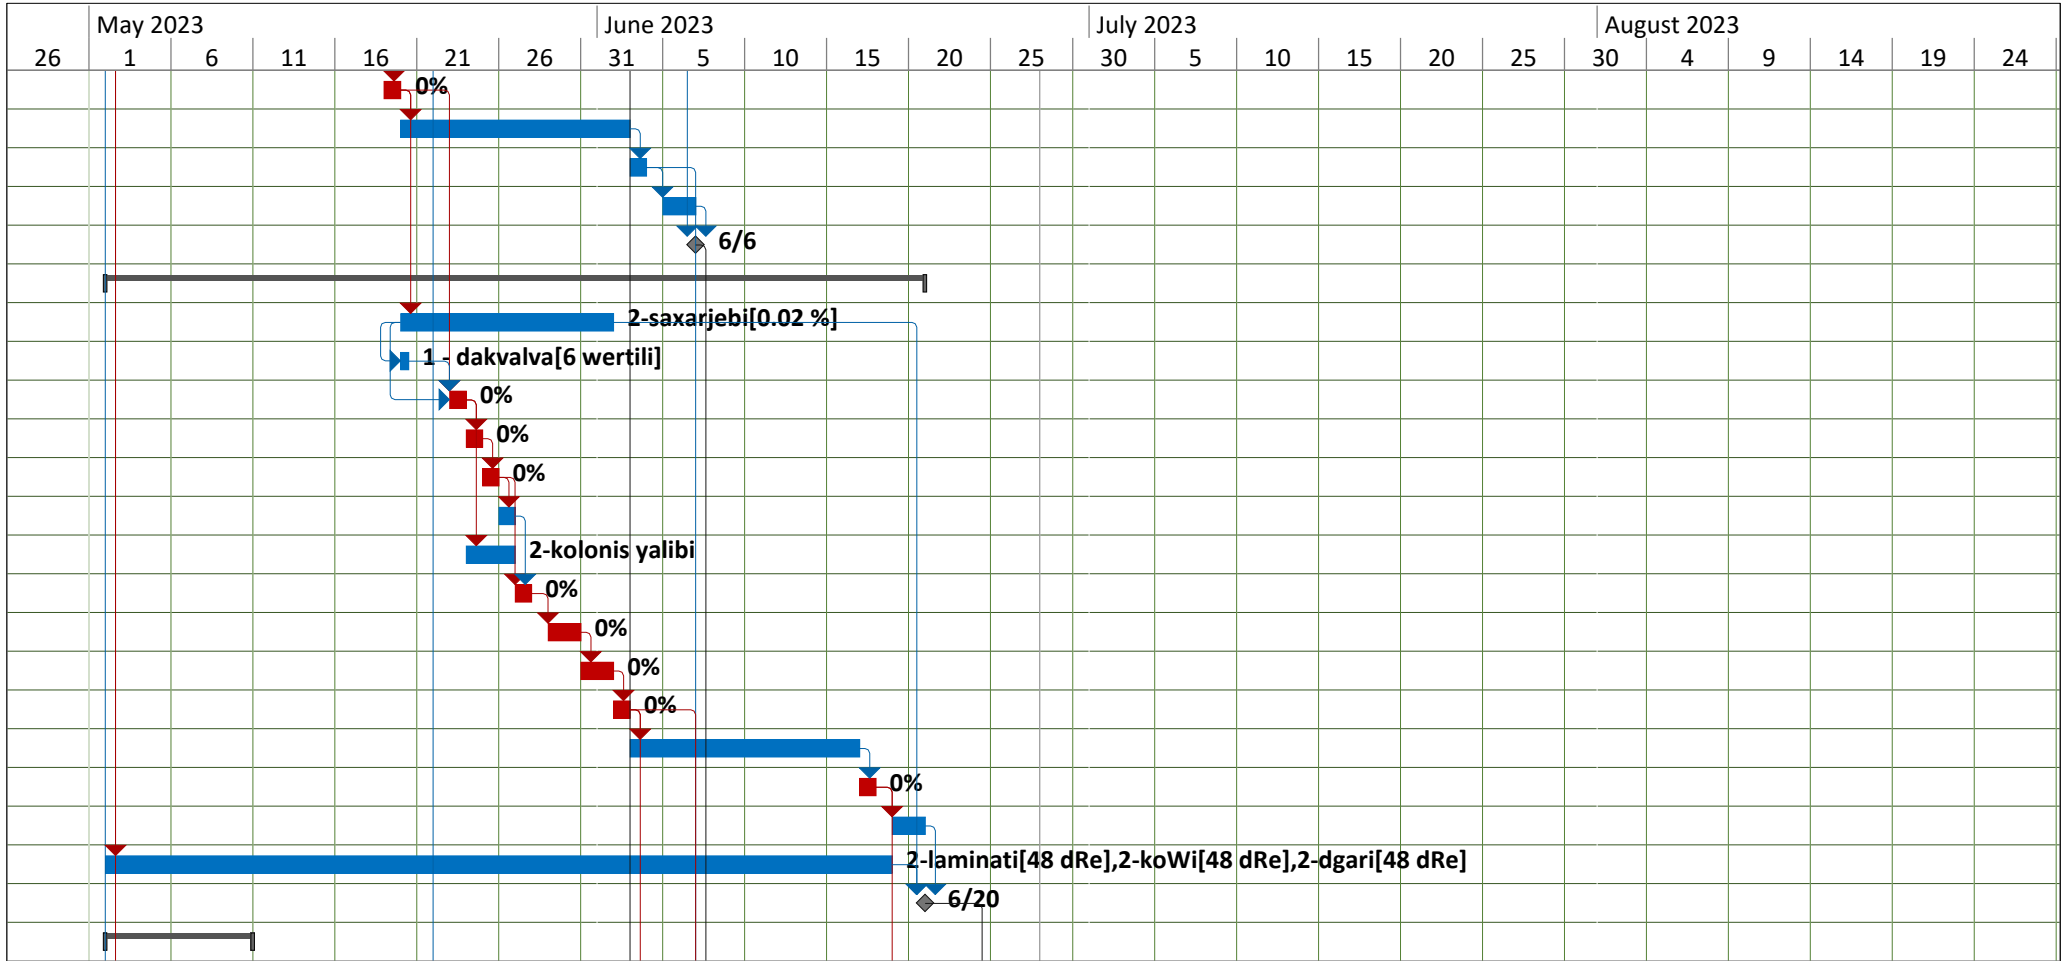

Project: msproj11
Date: Thu 3/23/23

Task		Inactive Task		Start-only	
Split		Inactive Milestone		Finish-only	
Milestone		Inactive Summary		Deadline	
Summary		Manual Task		Critical	
Project Summary		Duration-only		Critical Split	
External Tasks		Manual Summary Rollup		Progress	
External Milestone		Manual Summary		Manual Progress	

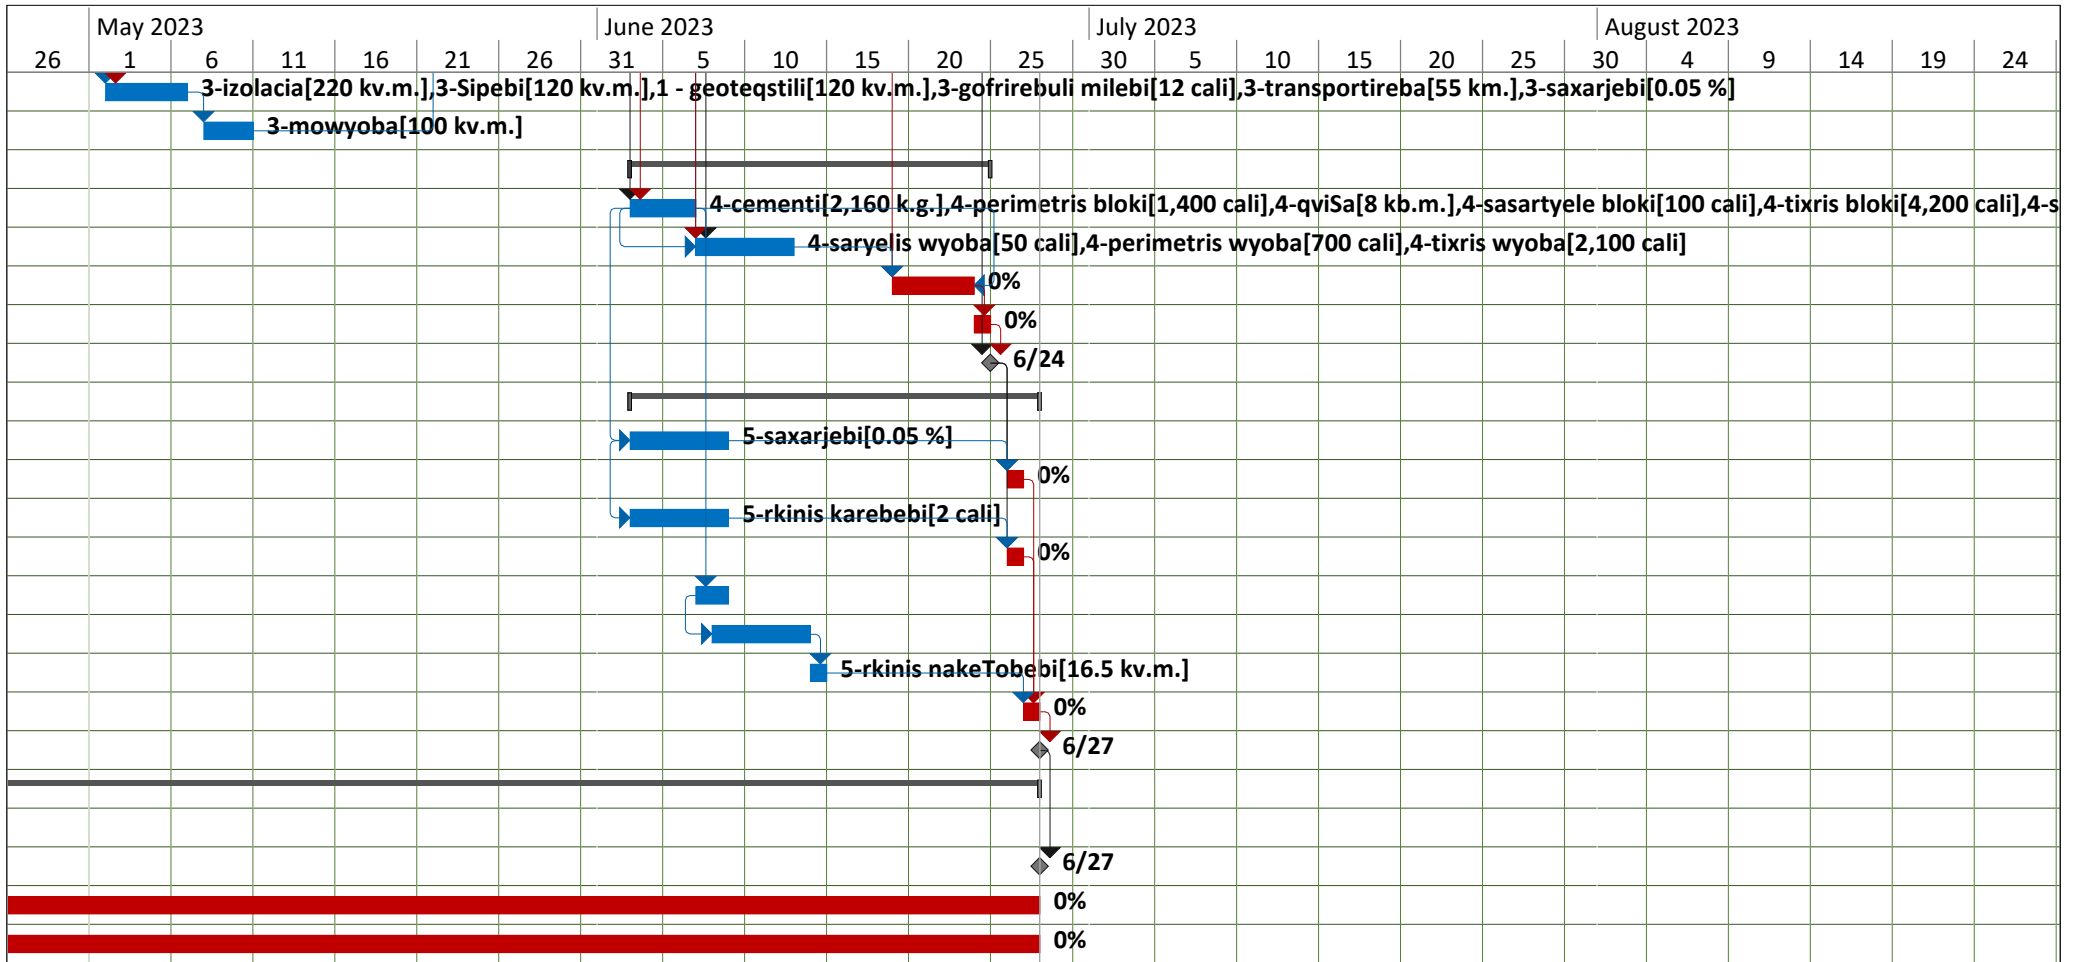

Project: msproj11 Date: Thu 3/23/23	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Critical	
	Project Summary		Duration-only		Critical Split	
	External Tasks		Manual Summary Rollup		Progress	
	External Milestone		Manual Summary		Manual Progress	

May 2023							June 2023							July 2023							August 2023						
26	1	6	11	16	21	26	31	5	10	15	20	25	30	5	10	15	20	25	30	4	9	14	19	24			
0%																											
0%																											



Project: msproj11 Date: Thu 3/23/23	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Critical	
	Project Summary		Duration-only		Critical Split	
	External Tasks		Manual Summary Rollup		Progress	
	External Milestone		Manual Summary		Manual Progress	
